# Site Validation Report

## Upson

92 Ben Hill Rd
Thomaston, GA 30286

### SITE

| AC System Size | DC System Size | Valid Data Date |
|---|---|---|
| 3,000 | 3,727 | 3/3/2023 |

### PRODUCTION HIERARCHY

| Inverters | Strings | Modules |
|---|---|---|
| 24 | 258 | — |

### RULE TOOL RESULTS

| Category | Rule | Result | Success % |
|---|---|---|---|
| Communication | Network Communication | Pass | 100 |
| | Upload | Pass | 100 |
| | Availability | Pass | 100 |
| | Inverter Uptime | Pass | 100 |
| Configuration | System Size | Pass | 100 |
| | PV Model | Pass | 100 |
| | WS & PV Model | Pass | 100 |
| | Default Alerts | Fail | 0 |
| | Hardware Configuration | Pass | 100 |
| | Site Configuration | Pass | 100 |
| | Alert Recipients | Pass | 100 |
| | Invalid Alerts | Pass | 100 |
| Data | Meter vs. Inverter Energy | Pass | 99 |
| | Power vs. Energy | Pass | 100 |
| | Meter Voltages | Pass | 100 |
| | Weather Station Data | Fail | 0 |
| | Data Curation | Pass | 100 |
| | Meter CT Check | Fail | 100 |

## PERFORMANCE




| Total Production | Expected Production* | Energy Ratio |
|---|---|---|
| 13,200 kWh | 24,569 kWh | 54 % |

*Expected production is based on Stem's PV model and weather data.

### Inverter Energy Ratio*

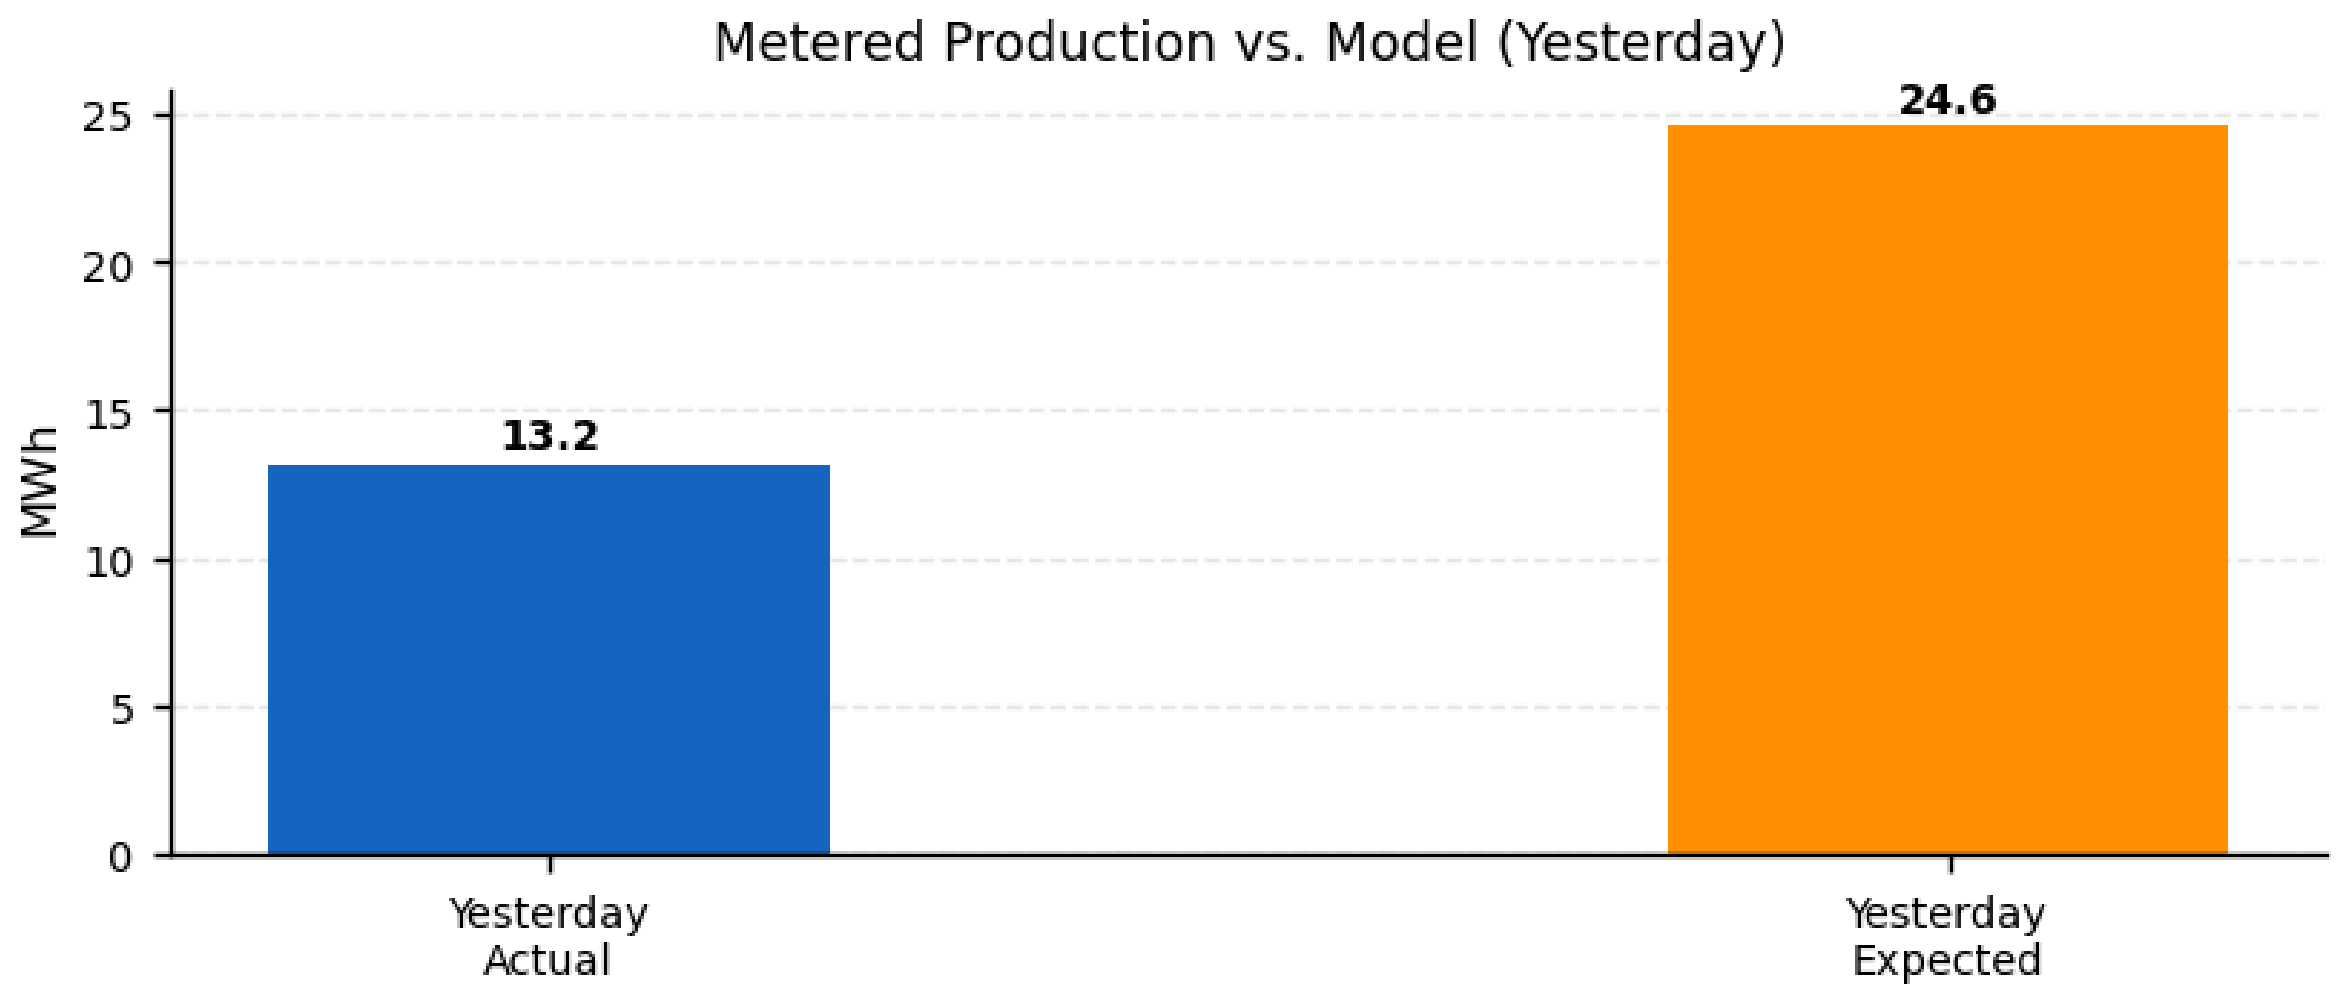


*Inverter Energy Ratio is based on Stem's PV model and weather data.

## RULE TOOL INFORMATION

| | |
|---|---|
| **Network Communication:** | Identifies local network failures by identifying common communication problems on devices connected via TCP and R |
| **Upload:** | Verifies that all devices have uploaded recently. Most devices are expected to upload at least once every 15 minutes. |
| **Availability:** | Verifies that there are no gaps in the 15-minute data from all devices. |
| **System Size:** | Verifies that system size is set on the site and inverters. |
| **PV Model:** | Verifies that the PV model is completely configured for every inverter. |
| **WS & PV Model:** | Makes sure that irradiance and module temperature data are available from the weather stations on the site. |
| **Default Alerts:** | Verify that the devices are configured with the default alerts. |
| **Hardware Configuration:** | Check a number of hardware configuration details, including alerts settings, PV and DC combiner output settings and |
| **Site Configuration:** | Check a number of site configuration details, including: Latitude, longitude, time zone, Allow alert email and Limited co |
| **Alert Recipients:** | Make sure alerts are set up to be generated from this site and that there is at least one alert notification recipient. |
| **Meter vs. Inverter Energy:** | Verifies that the energy measurements correlate between each production meter and the inverters connected to it. |
| **Power vs. Energy:** | Verify that the integral of the power matches the energy to within 10%. This test is run individually on each inverter an |
| **Meter Voltages:** | Makes sure that the phase voltages are within 5% of each other. |
| **Weather Station Data:** | Verifies that temperature and irradiance data is within expected ranges. Checks temperature variation, ambient vs. mo |

Rule Tool checks the past 24 hours for pass/failure

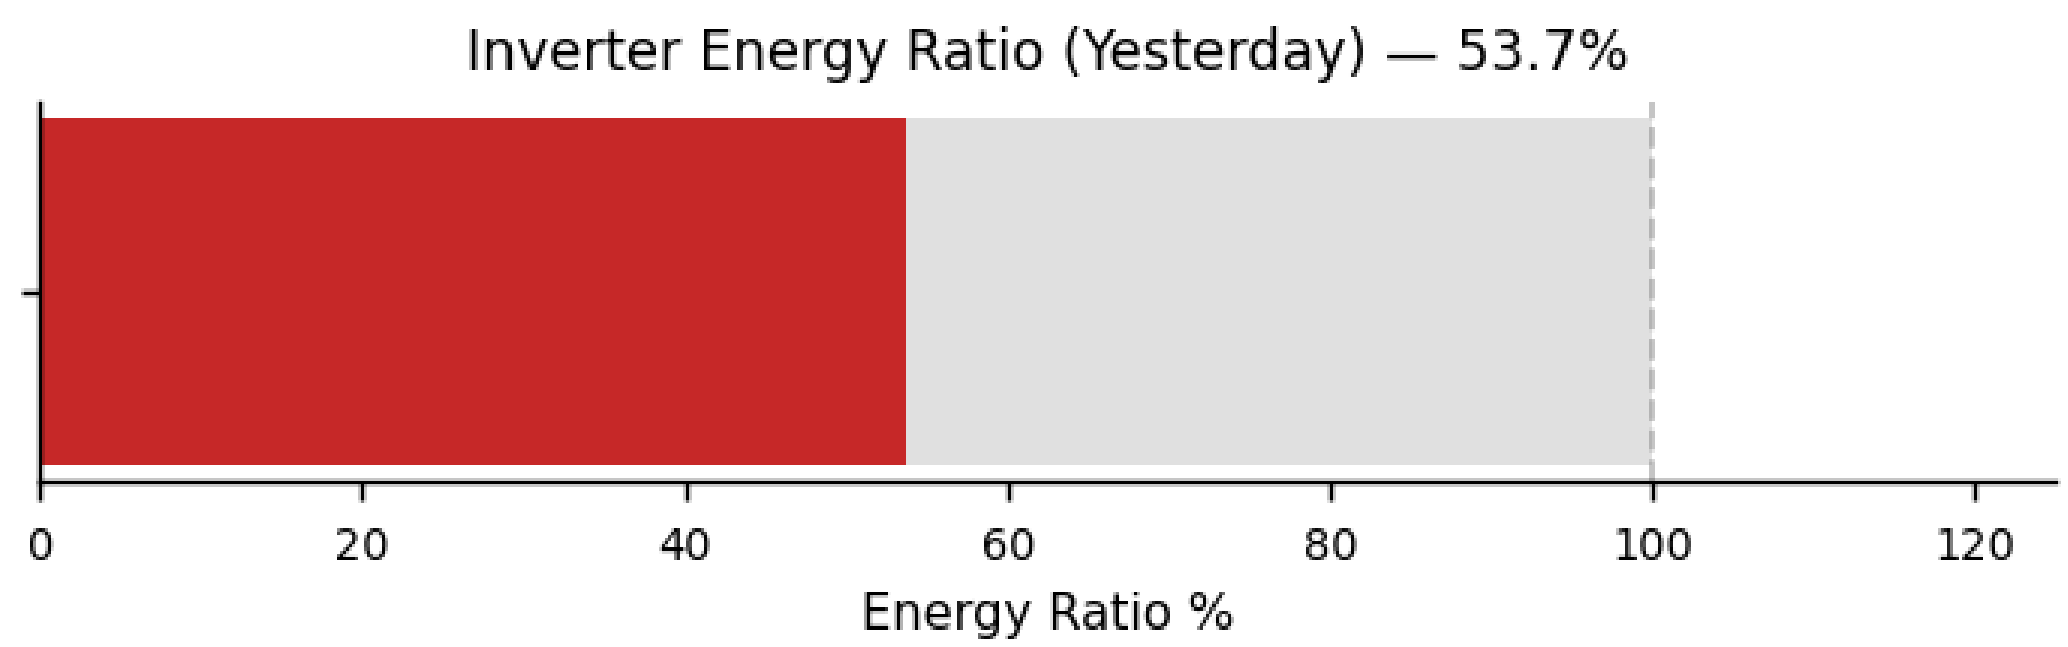View the complete rule tool checklist and other site information via Powertrack: apps.alsoenergy.com
